BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
1	Providing and constructing load bearing wall with solid concrete blocks having block density not less than 1800kg/m3 having a minimum average compressive strength of 5.00 N/mm2 confirming to IS 2185 (Part 1):2005 and	Sqm	868.12	226.43	26	30-01-21	24-02-21	25
2	Providing and laying in position reinforced cement concrete of Design Mix M20 with OPC @ 320kgs, with 20mm and down size graded granite metal course aggregates @0.69cum and fine aggregates@ 0.460 cum,	Cum	4.80	3.35	70	30-01-21	04-02-21	5
3	Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and I or welding wherever required, tying with binding wire and anchoring to the adjoining	tonne	11.11	5.78	52	26-12-20	25-03-21	89
4	Providing 15mm thick plain plastering in single coat to external masonry surfaces, in cement mortar 1:4 (1 cement : 4 fine sand) including providing & mixing water proofing compound of approved quality and	Sqm	2233.23	146.49	7	04-02-21	01-03-21	25
5	Providing and finishing external walls in two coats with waterproof cement paint of approved brand and shade to give an even shade after thoroughly becoming the surface to remove all dirt and loose powdered material, free from mortar	Sqm	3828.31	2995.33	78	14-02-21	11-03-21	25
6	Providing barbed GI wire fencing of 12x12 gauge drawn into stone pillars or iron pillars including drawing in holes wherever necessary excluding the cost of pillars but including the cost of barbed wire and binding wire etc.	m	18554.34	173.29	1	02-02-21	12-02-21	10
10	Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.87t cum and fine aggregates @ 0.55cum, machine mixed,	Cum	86.49	17.68	20	25-01-21	05-02-21	11
13	Providing applying two coats of wall putty to inside plastered walls and ceiling using white cement putty. Scrapping and levelling the surface using steel blade and preparing the surface even and smooth by using	Sqm	950.53	2875.34	100	15-03-21	30-03-21	15

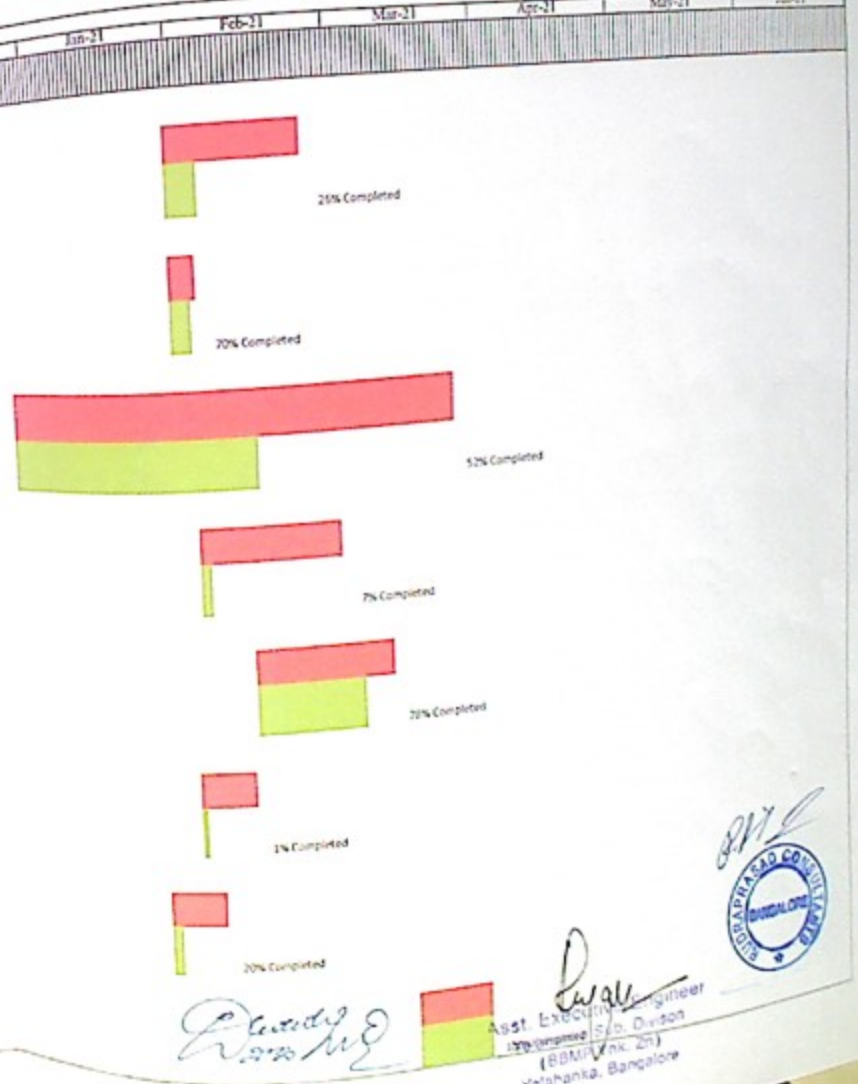

RUDRAPRASAD CONSULTANTS BANGALORE

Asst. Executive Engineer
ISD Division
(BBMP Wrk. Zn)
Yelahanka, Bangalore

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
14	Providing and applying two coats with oil bound washable distemper of approved brand and shade on wall surface including priming coat with distemper primer after throughly brooming the surface free from mortar	Sqm	5835.74	1881.91	32	18-03-21	02-04-21	15
16	Providing and finishing external walls in two coats with waterproof cement paint of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar	Sqm	2441.10	636.28	26	21-03-21	05-04-21	15
17	Providing and finishing external walls in two coats with waterproof cement paint of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar	Sqm	730.13	601.50	82	23-03-21	07-04-21	15
18	Applying red lead ready mix priming coat over new steel or other metal surface including preparing the surface after throughly cleaning oil, grease, dirt and other foreign matter, and scoured with wire brushes, fine steel wool, sand	Sqm	1249.60	690.08	55	02-04-21	17-04-21	15
19	Applying red lead ready mix priming coat over new steel or other metal surface including preparing the surface after throughly cleaning oil, grease, dirt and	Sqm	348.57	585.20	100	03-04-21	18-04-21	15
20	Applying red lead ready mix priming coat over new steel or other metal surface including preparing the surface after throughly cleaning oil, grease, dirt and other foreign matter, and scoured with wire brushes, fine steel wool, sand	Sqm	42.00	331.87	100	25-04-21	30-04-21	5
21	Providing and applying enamel metal paint one coat (excluding priming coat) on previously painted steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost	Sqm	1249.60	690.08	55	07-04-21	27-04-21	20
22	Providing and applying enamel metal paint one coat (excluding priming coat) on previously painted steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other	Sqm	348.57	585.20	100	08-04-21	28-04-21	20

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Dnk. Zn)
Yelahanka, Bangalore

BRUHAT BENGALURU MAHANAGARA PALIKE

ents Name	:	Executive Engineer, Yelahanka Division.
oject Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
onsultants	:	Rudraprasad Consultants
roject Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
	Providing and applying enamel metal paint one coat (excluding priming coat) on previously painted steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost of	Sqm	42.00	956.14	100	24-04-21	30-04-21	6
24	Applying priming coat over new wood surface and / or wood based surface with white lead paint priming including preparing the surface after thoroughly cleaning oil, grease, dirt and foreign matter, sand papering and knotting ready mix paint including cost	Sqm	282.74	248.17	88	21-04-21	27-04-21	6
25	Providing and applying painting one coat (excluding priming coat) on previously painted wood surface and I or wood based surface with enamel paint to give an even shade after cleaning the surface of all dirt, dust and foreign	Sqm	282.74	248.17	88	22-04-21	28-04-21	6
27	Dismantling the tile work in floor and roof laid in cement or surki mortar including stacking the materials with in 50 m lead of tiles thickness 10mm to 25mm. including cost of materials, labour, HOM complete as per	Sqm	849.71	378.02	44	08-04-21	18-04-21	10
28	Dismantling weather proof course and removing and conveying the debris to a distance upto 200m. including cost of materials, labour, HOM complete as per specifications and directions of Engineer-in-Charge	Cum	121.80	56.70	47	23-04-21	28-04-21	5
29	Providing and constructing burnt brick masonry with approved quality of modular bricks of standard size of class designation 5.0 Newton per sqmm (table moulded) with cement mortar 1 :8 for basement and	Cum	6.62	12.02	100	02-02-21	22-02-21	20
30	Fabrication supplying and erecting M.S. tubular trusses of all spans as per approved drawing & design with prefabricated steel applications using quality material and are durable, reliable and corrosion and abrasion resistant.	kg	16200.00	14380.83	89	10-04-21	20-04-21	10
31	Providing and fixing 6mm cl ear I opal white I solar I bronze I blue I green tinted multi wall poly carbonate sheet for tubular structure. The work including cost of all materials, labour charges and hire charges of machineries for	Sqm	555.60	624.28	100	13-04-21	21-04-21	10

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
32	Providing and fixing to wall, ceiling and floor unplasticised PVC 6.00 kgs/sqcm working pressure with pipe fittings, wall clips etc., and making good the wall, ceiling and floor for sanitary pipelines including cost of all materials, labour	m	85.00	74.60	88	26-03-21	31-03-21	5
33	Providing and fixing Vitrified glazed tiles of approved make, quality & colour of size 900 x 900 x 12mm thick fixed on bed of 12mm thick cement mortar for flooring, skirting and jointed with neat cement slurr mixed with pigment to	Sqm	630.49	122.69	19	24-03-21	23-04-21	30
34	Providing and fixing in position aluminium windows and ventilators as per approved drawings with sliding shutters using three track window frame of size 92x31 75mm bottom section 1 3mm thick, Weight 1 07kg/m, sides and top sections	Sqm	633.00	285.54	45	15-02-21	07-03-21	20
35	Providing and fixing M.S grill work for windows and ventilators using M.S. flats, or M.S. square rods, or combination of M S flats and square rods as per approved design, drawing including cutting steel sections and welding the	kg	8990.10	332.01	4	09-03-21	19-03-21	10
38	Providing and constructing load bearing wall with solid concrete blocks having block density not less than 1800kg/m3 having a minimum average compressive strength of 5.00 N/mm2 confirming to IS 2185 (Part 1):2005 and constructed with	Sqm	17.76	106.41	100	15-02-21	12-03-21	25
49	Providing and applying two coats with oil bound washable distemper of approved brand and shade on wall surface including priming coat with distemper primer after thoroughly brooming he surface free from mortar drops and other	Sqm	1250.97	2098.95	100	25-03-21	29-04-21	35
41	Providing and laying platform using prepolished, water cut 1 gang saw 40mm thick telephonic Black Granite laid on existing vertical -supports and fixing in CM 1 3 proportion Including cutting to required shape, pattern with paper joints	Sqm	33.50	24.29	72	25-03-21	14-04-21	20
42	Providing and laying platform using prepolished, water cut 1 gang saw 40mm thick telephonic Black Granite laid on existing vertical -supports and fixing in CM 1 3 proportion. Including cutting to required shape, pattern with paper joints,	Sqm	41.60	16.51	40	30-03-21	19-04-21	20

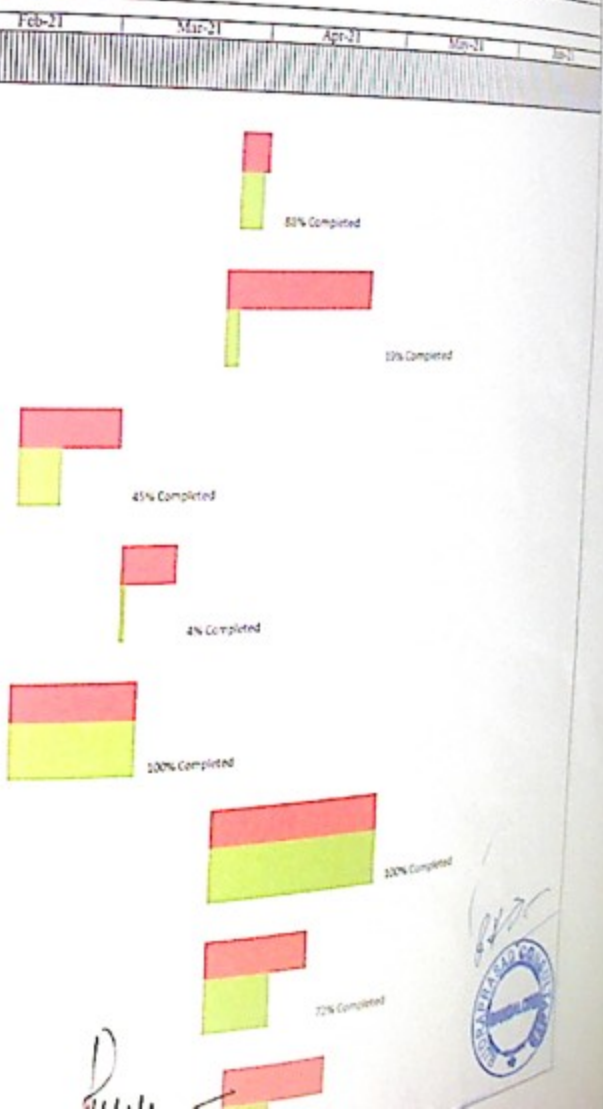

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
63	Construction of dry lean cement concrete mix CC 1:5:10 with OPC cement @160Kgs, with 25mm and down size graded granite metal course aggregate at 0.86cum	Cum	135.00	216.16	100	28-01-21	11-02-21	14
64	Constructing un-reinforced, plain cement concrete for pavements using Grade concrete M10 over a prepared base with OPC course aggregate at 0.69 cum, fine aggregates at 0.46 cum,Course and fine aggregate	Cum	270.00	288.21	100	08-02-21	22-02-21	14
70	Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be levelled neatly after breaking of clods complete as per specifications	Cum	64.20	3.85	100	09-02-21	17-02-21	8
71	Plain cement concrete M10 mix with crushed stone aggregate 40mm nominal size mechanically mixed, placed in foundation and compacted by vibration including curing including cost of materials, labour.	Cum	10.78	1.28	100	10-02-21	20-02-21	10
72	Providing and fixing pre cast solid cement concrete kerb stones made out of C.C. 1:2:4 with top and bottom width 114 and 165 mm respectively. 400mm high and 450mm in length finished with CM 1:3 plastering and finishing cutting.	m	488.85	143.00	29	10-02-21	20-02-21	10
73	Painting two coats after filling the surface with synthetic enamel paint in approved shades on new plastered concrete surfaces, with materials, labour complete as per specifications	Sqm	59.40	25.66	43	15-02-21	25-02-21	10
74	Providing T.M.T steel reinforcement for R.C.C. work including straightening, cutting, bending, hooking, placing in position, lapping and/or welding wherever required, tying with binding wire and anchoring to the adjoining members	Tonne	1.12	23.66	100	24-01-21	20-02-21	27
77	Earthwork excavation by manual means for foundation of buildings, water supply and sanitary lines and electrical conduits etc, either in pits or in trenches 1.5m and above in width, in soil not exceeding 1.5 m. in depth including dressing the bottom	Cum	71.91	78.76	100	19-12-20	24-12-20	5

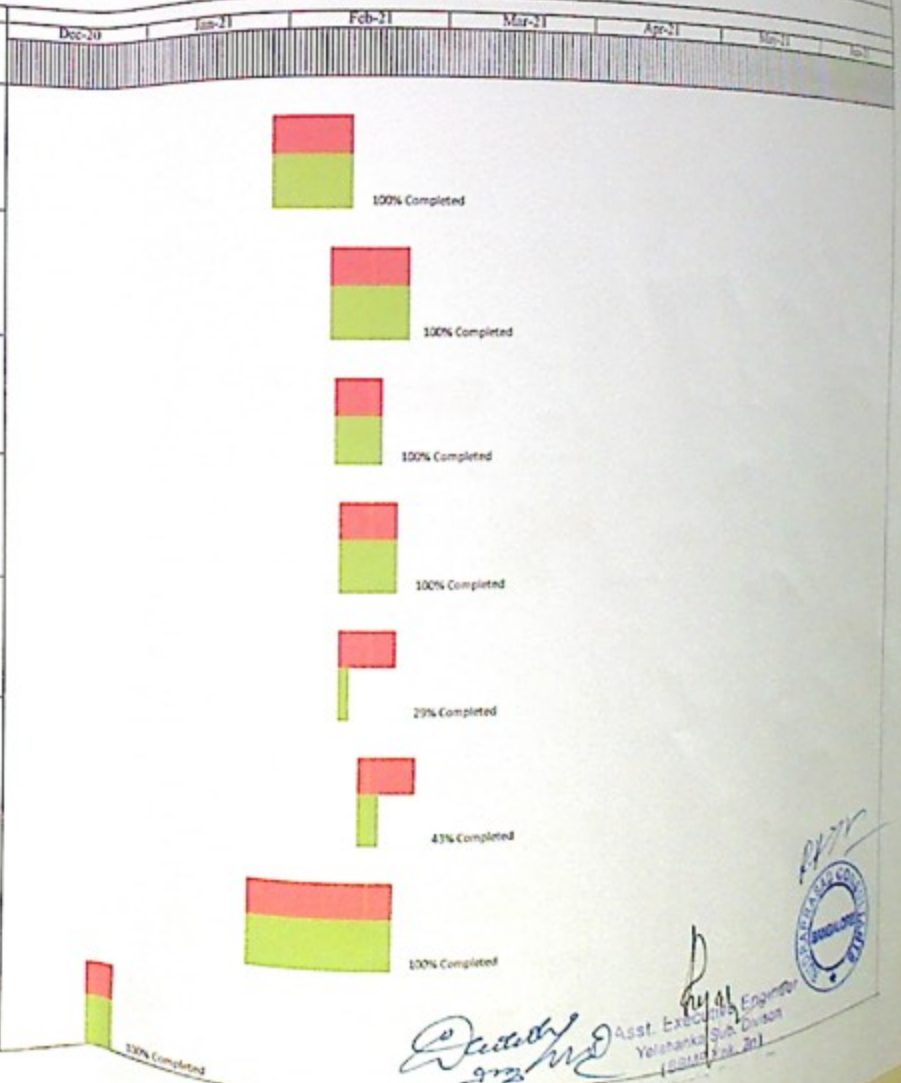

Asst. Executive Engineer
Yelahanka Sub. Division

BRUHAT BENGALURU MAHANAGARA PALIKE

ients Name	:	Executive Engineer, Yelahanka Division.
roject Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
114	Providing Ceramic tiles of approved make,shade and size for flooring, treads of steps and landings laid on a bed of 12mm thick, cement mortar 1:3 mix, flush pointing with white cement using colour pigment , including cost of materials,	Sqm	82.47	104.45	100	30-03-21	29-04-21	30
115	Providing rough cement-plastering15mm thick in single coat with cement mortar to brick masonry for base of dadooing works with sand of approved quality, providing and removing scaffolding, including cost of materials, labour,	Sqm	526.37	614.43	100	29-03-21	29-04-21	31
116	Providing skirting, dadoing, rises of steps with colour glazed tiles on 10mm thick cement plaster 1:3 and jointed with white cement slurry over existing rough plaster surface using glazed tiles of approved make and size including cost of	Sqm	263.19	198.43	75	02-04-21	02-05-21	30
117	Providing skirting, dadoing, rises of steps with colour glazed tiles on 10mm thick cement plaster 1:3 and jointed with white cement slurry over existing rough plaster surface using glazed tiles of approved make and size including cost	Sqm	263.19	198.79	76	29-03-21	29-04-21	31
118	Providing wood frames of doors, windows, clerestorywindows, ventilators and other frames, wrought, framed or assembledincluding making plaster groves (excluding cost of cement concrete andside clamps),	Cum	0.18	0.09	50	10-04-21	20-04-21	10
119	Providing wood frames of doors, windows, clerestorywindows, ventilators and other frames, wrought, framed or assembledincluding making plaster groves (excluding cost of cement concrete andside clamps), but including	Cum	0.08	0.09	100	10-04-21	20-04-21	10
120	Providing and fixing PVC Hollow Door Frame of the size 50x47mm with a wall thickness of 5mm, made out of extruded 5mm rigid PVC foam sheet, mitre cut at two corners and joined with 2 Nos. of 150mm long brackets of 15x15mm	m	178.65	99.00	55	12-04-21	22-04-21	10
121	Providing and fixing PVC Hollow Door Frame of the size 50x47mm with a wall thickness of 5mm, made out of extruded 5mm rigid PVC foam sheet, mitre cut at two corners and joined with 2 Nos. of 150mm long brackets of 15x15mm	m	118.75	99.00	83	12-04-21	22-04-21	10

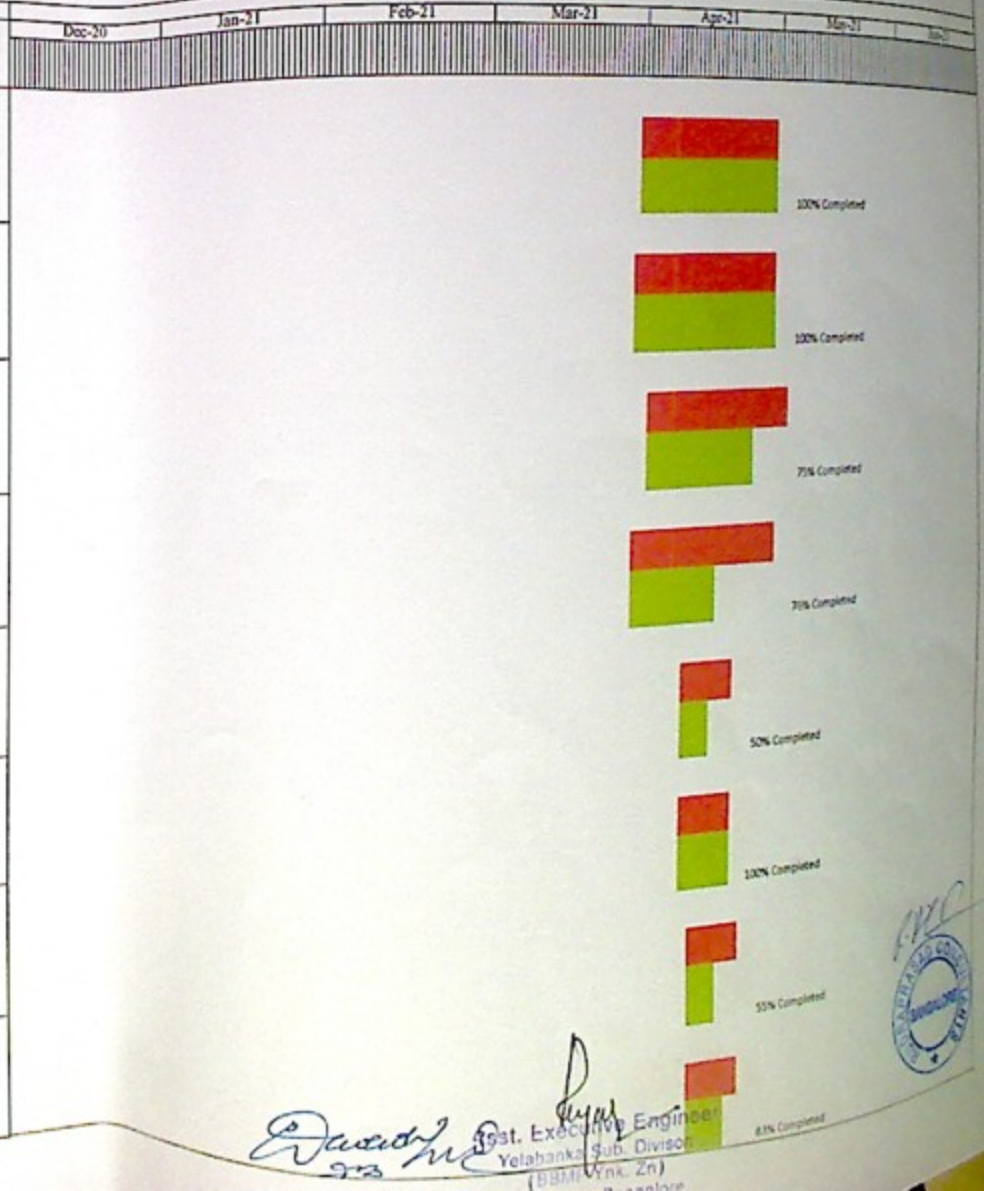

Asst. Executive Engineer
Yelahanka Sub. Division
(BBMP/Ynk. Zn)

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer, Yelahanka Division.
Project Name	:	"Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division."
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
139	Wall Mounted Soap Dispenser- Stainless steel. Complete as per specifications and directions of Engineer-in-Charge	Each	16.00	3.00	19	17-04-21	27-04-21	10
140	Paper Towel Dispenser-holder Complete as per specifications and directions of Engineer-in-Charge	Each	16.00	5.00	31	20-04-21	30-04-21	10
141	Sanitary Napkin Burning Machin Complete as per specifications and directions of Engineer-in-Charge	Each	6.00	3.00	50	21-04-21	26-04-21	5
142	Providing & applying water proofing to concrete surfaces using high quality polymer-modified bituminous compounds (confirming to ASTM Spn D 5147) reinforced with non woven polyester fabric, weighing	Nos	2.00	2.00	100	09-04-21	19-04-21	10
146	Supplying heavy gauge PVC conduit pipe ....mm dia .....mm thick confirming to IS 2509 with suitable size bends, metal/PVC junction boxes, adhesive paste etc., and running before concreting the slab. The conduit	mtrs	200.00	200.00	100	30-03-21	09-04-21	10
147	Supplying heavy gauge PVC conduit pipe ....mm dia .....mm thick confirming to IS 2509 with suitable size bends, metal/PVC junction boxes, adhesive paste etc., and running before concreting the slab. The conduit	mtrs	160.00	160.00	100	02-04-21	10-04-21	8
148	Supplying heavy gauge PVC Conduit Pipe ...dia .....mm thick with suitable size bends, metal junction boxes adhesive paste etc., by groove cutting in the wall and fixing by bracing U or J hooks and cement plastering up to	mtrs	50.00	50.00	100	04-04-21	12-04-21	8
149	Supplying heavy gauge PVC Conduit Pipe ...dia .....mm thick with suitable size bends, metal junction boxes adhesive paste etc., by groove cutting in the wall and fixing by bracing U or J hooks and cement plastering up to	mtrs	50.00	50.00	100	06-04-21	14-04-21	8

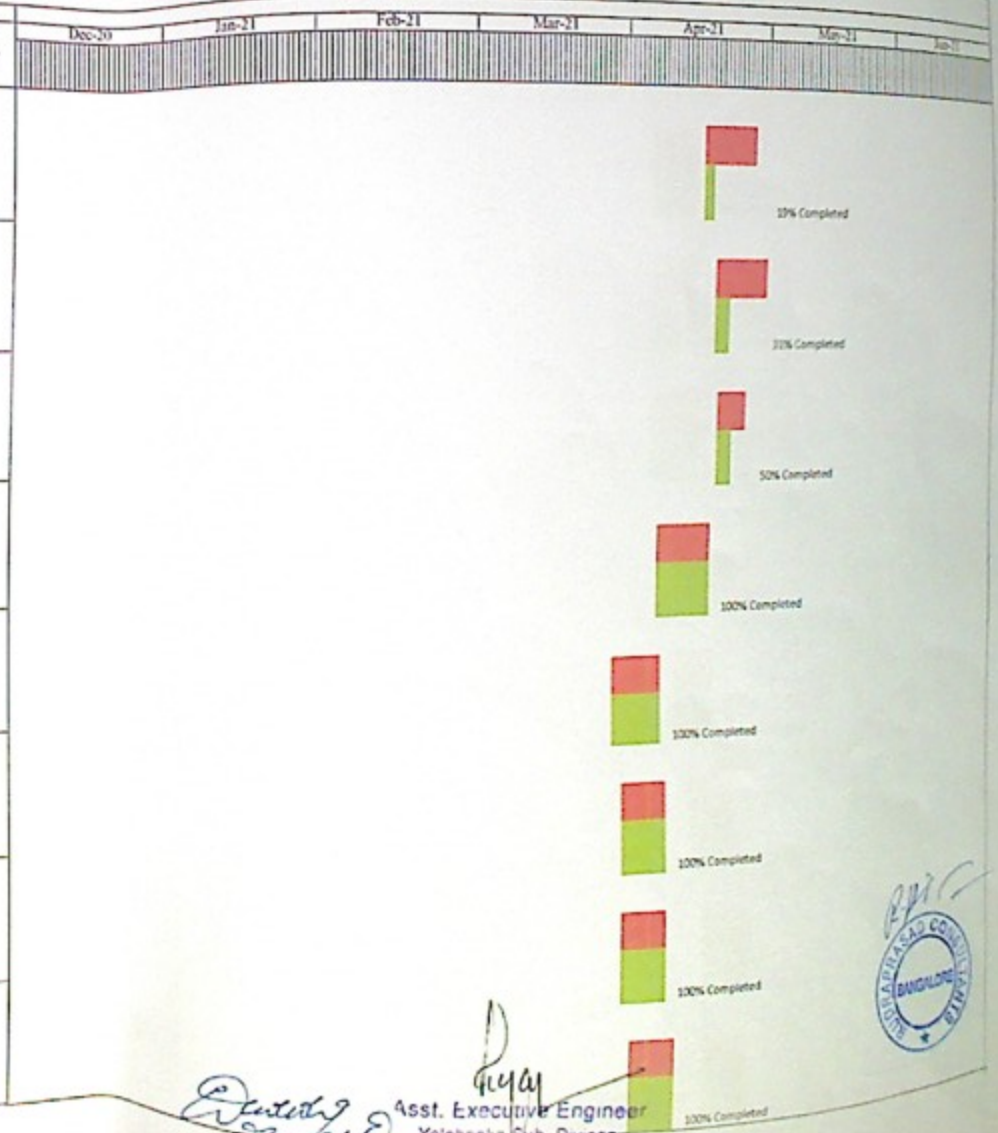

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Ynk. Zn)
Yelahanka, Bangalore

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Divison.
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
166	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos. of machine screws, bolts nuts etc., complete on the existing metal/PVC	Nos	8.00	8.00	100	23-04-21	30-04-21	7
167	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos. of machine screws, bolts nuts etc., complete on the existing metal/PVC	Nos	8.00	8.00	100	21-04-21	28-04-21	7
168	Supplying and fixing superior quality modular switch mounting polycarbonate plate with necessary supporting back plate with required nos. of machine screws, bolts nuts etc., complete on the existing metal/PVC	Nos	4.00	4.00	100	22-04-21	30-04-21	8
169	Supplying and fixing of modular switch & connected accessories on existing modular switch plate as per IS 3854 and IS 1293. 6Amps one way Switch. Complete as per specifications and directions of Engineer-in-Charge.	Nos	50.00	50.00	100	22-04-21	30-04-21	8
170	Supplying and fixing of modular switch & connected accessories on existing modular switch plate as per IS 3854 and IS 1293. 16Amps one way switch. Complete as per specifications and directions of Engineer-in-Charge.	Nos	4.00	4.00	100	23-04-21	01-05-21	8
171	Supplying and fixing of modular switch & connected accessories on existing modular switch plate as per IS 3854 and IS 1293. 6/16Amps universal socket. Complete as per specifications and directions of Engineer-in-Charge.	Nos	40.00	20.00	50	21-04-21	29-04-21	8
172	Supplying, fixing and wiring Earth Leakage Miniature Circuit Breaker (ELMCB) 240/450V up to 300mA sensitivity on existing wood/panel board. 16-25 Amps 2 pole. Complete as per specifications and directions of	Nos	2.00	2.00	100	21-04-21	26-04-21	5
173	Supplying and fixing miniature circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' Type curve, indicator ON/OFF, energy cross-3 with/Short circuit breaking capacity of 10K and complete	Nos	12.00	12.00	100	19-04-21	29-04-21	10

Asst. Executive Engineer
Yelahanka Sub. Divison

RUDRAPRASAD CONSULTANTS BANGALORE

BRUHAT BENGALURU MAHANAGARA PALIKE

Clients Name	:	Executive Engineer Yelahanka Division
Project Name	:	Development and Construction of Auditorium and Toilet at Yelahanka PU Collage in Ward No-01 of Yelahanka Sub Division
Consultants	:	Rudraprasad Consultants
Project Manager /Team Leader	:	Karthik Rechan
Project Start Date	:	19-Dec-20
Project End Date	:	17-Jun-21
Project Length in Months	:	180 Days

Sl. No	Assignment	Unit	Tender Qnty	Qty of Work done	% Of Work done	Start Date	End Date	No. of Working Days
E1	Providing and fixing granite flooring in combination of 19mm thick (Avg) gang saw water cut LAKARED granite with 86% and with 14% of 19mm thicl (avg) Black granite in CM 1:4 proportion with a coat of rough plastering using CM 1:4,	Sqm	558.35	558.35	100	15-04-21	30-04-21	15
E2	Providing and fixing granite flooring in combination of 19mm thick (Avg) gang saw water cut LAKARED granite with 86% and with 14% of 19mm thicl (avg) Black granite in CM 1:4 proportion with a coat of rough plastering using CM 1:4,	Sqm	287.83	287.83	100	15-04-21	01-05-21	16
E3	Providing and fixing 12.5mm to 25 mm expanded metal work of 14 gauge with Mathi or Nandi wood patties of 50 mm x 12 mm size, including two coats approved paint etc., complete.	Sqm	138.56	138.56	100	05-02-21	20-02-21	15
E4	Providing and Fixing Stainless Steel sink of sizes above 60cms x 45cms in 20mm thick granite slab of by cutting required thickness and width of grooves and fixing using adhesives etc., complete including cost and	nos	260.91	260.91	100	15-04-21	01-05-21	16
E5	Providing and laying M-15 cement concrete flooring 60 mm thick with metallic concrete hardner toping, under layer of 45mm thick M-15 cement concrete using broken granite metal of 20mm and down size and top layer	Sqm	260.91	260.91	100	28-02-21	05-03-21	5
E6	Providing and laying M-15 cement concrete flooring 60 mm thick with metallic concrete hardner toping, under layer of 45mm thick M-15 cement concrete using broken granite metal of 20mm and down size and top layer of	Sqm	172.20	172.20	100	26-03-21	31-03-21	5

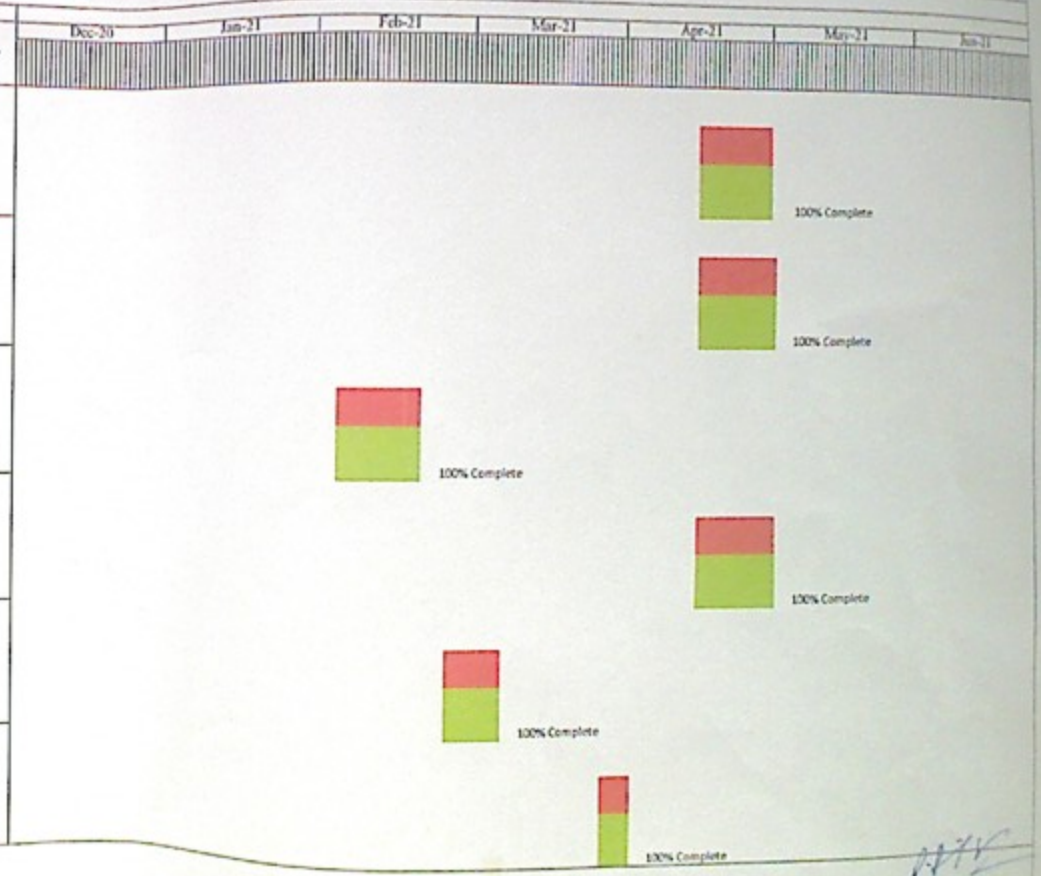

LEGEND

- Planned %
- Executed %

Asst. Executive Engineer
Yelahanka Sub. Divison
(BBMP Yak. Zn)
Yelahanka, Bangalore

RUDRAPRASAD CONSULTANTS BANGALORE
